



Brighton & Sussex University Hospital Clinical Administration Building






Delivery of outstanding modular units





Crane set up along
North Service Road

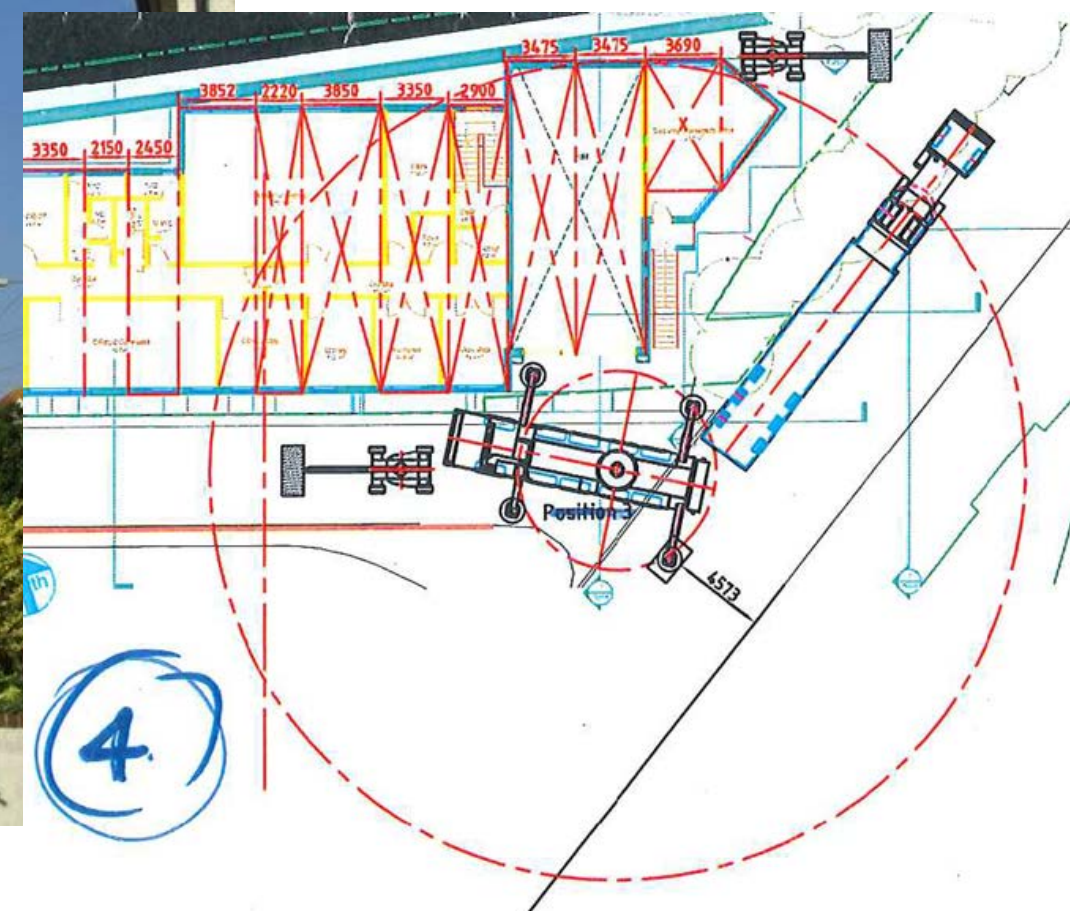



Suction excavator for
Infrastructure works

Temporary works for diamond drilling along North Service Road





Internal Office fit out works

Plant room fit out works



Summary

- Delivery of outstanding modular unit complete
- North Service Road closure Thursday 12th October to Wednesday 25th October 17
- Excavation underway along the North Service Road to install Infrastructure works from the Clinical Admin Building to existing hospital plant rooms
- Erection of scaffolding to commence for the external façade treatment
- Piling for earth rods on the East side complete
- Fuel tanks for the generators delivered
- Internal fit out works in progress
- Plant deliveries planned for this month
